DUNDONALD INTERNATIONAL ICE BOWL Outline Programme - Draft

22 April 2021
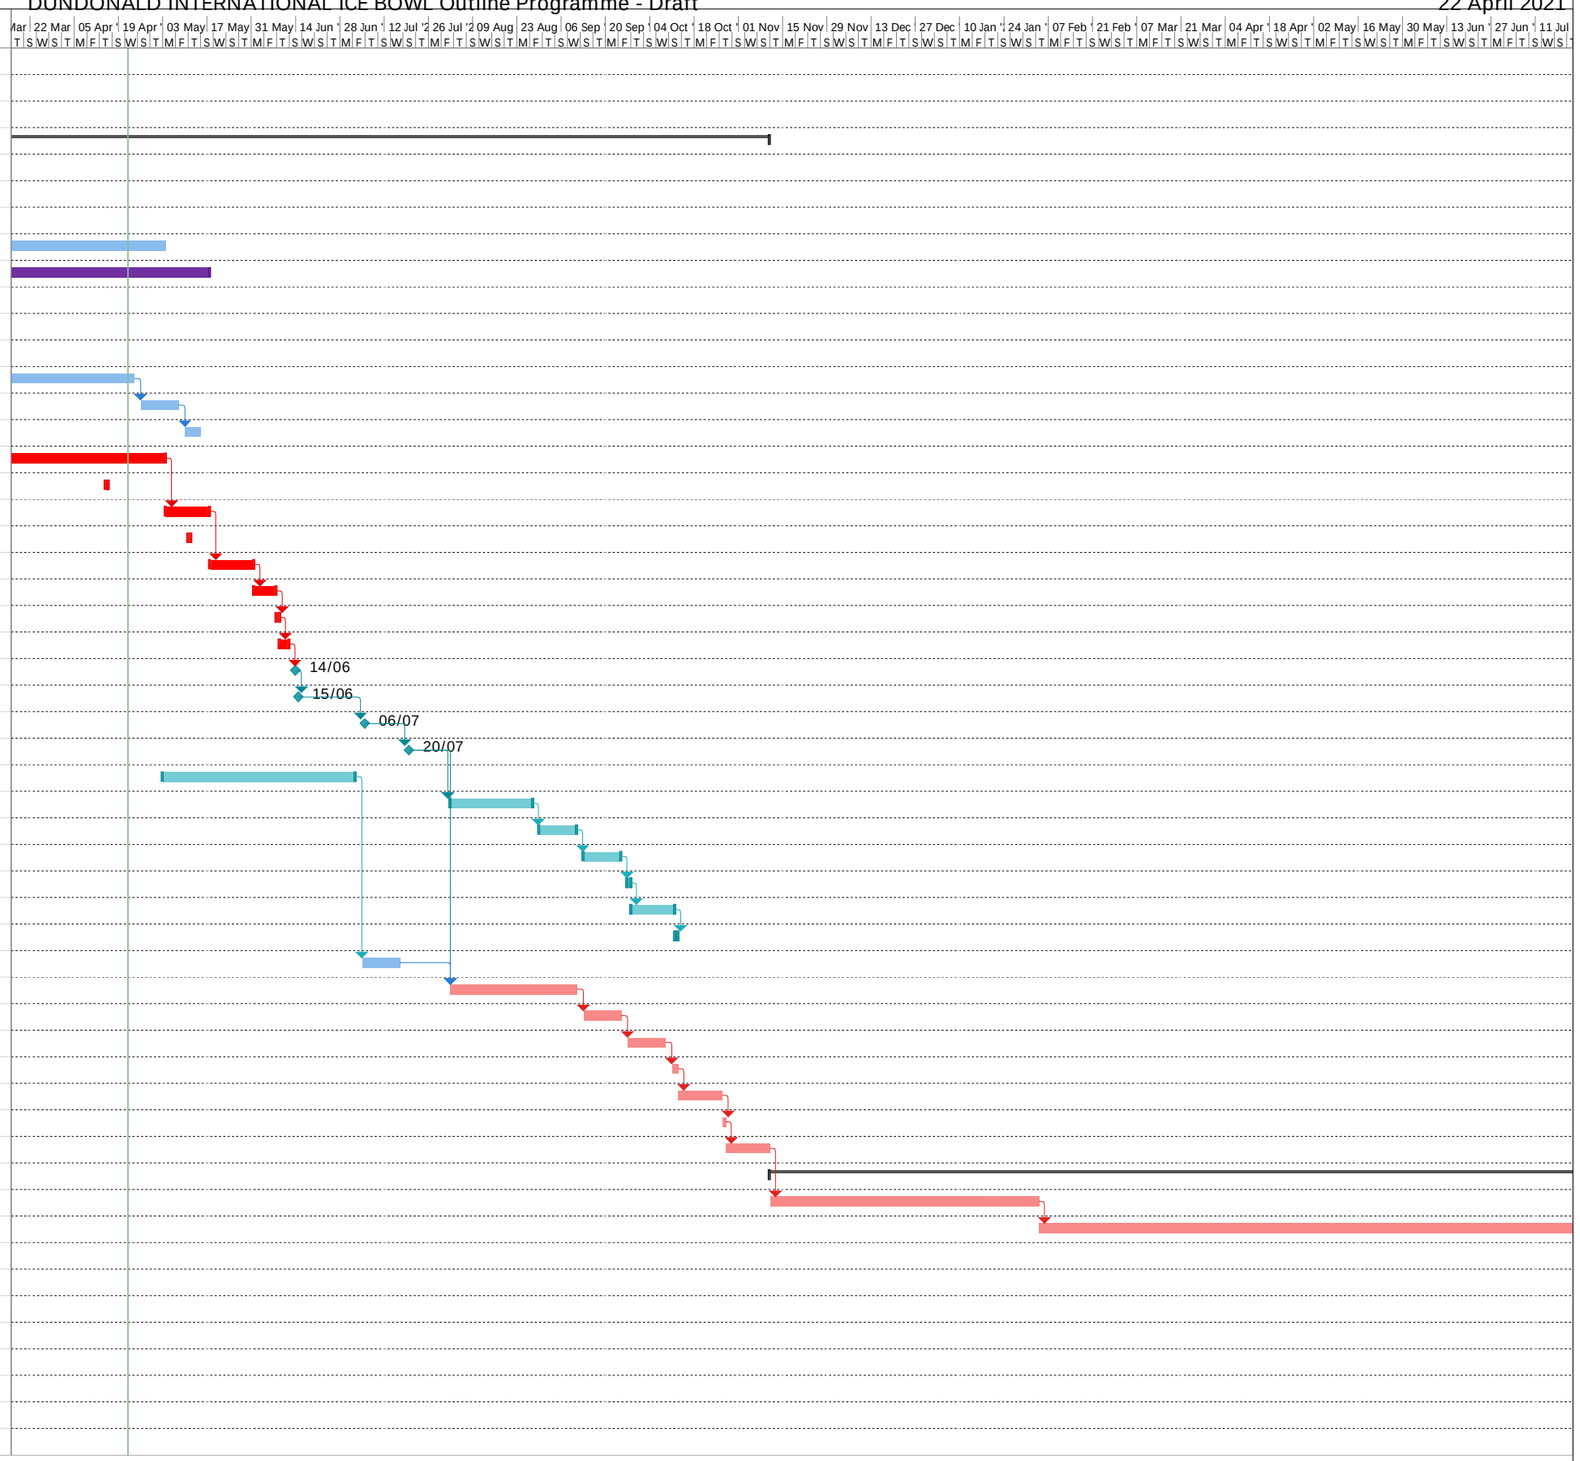
ID	Task Mode	Task Name	Duration	Start	Finish
1		**Stage 1 to Planning**	**345 days**	**Mon 12/02/18**	**Wed 26/06/19**
17		**RIBA Stage 2**	**253.5 days**	**Mon 03/09/18**	**Mon 09/09/19**
29		**RIBA Stage 3**	**255 days**	**Mon 15/07/19**	**Thu 23/07/20**
52		**RIBA Stage 4**	**438.5 days**	**Thu 20/02/20**	**Wed 10/11/21**
53		Technical Design & ITT documents (to be put on hold 30/10/20)	42 wks	Thu 20/02/20	Thu 17/12/20
54		EU Advert - Ice & Bowling	0 days	Fri 17/07/20	Fri 17/07/20
55		Procurement of Ice sub contractor (PQQ period)	9 wks	Mon 20/07/20	Fri 18/09/20
56		Procurement of Bowling sub contractor (PQQ period)	40 wks	Mon 20/07/20	Mon 03/05/21
57		Procurement (ITT) Hiatus 16/11/20 + 6months	125 days	Mon 16/11/20	Mon 17/05/21
58		Finalise PQQ documentation (Main Contract)	13 wks	Mon 20/07/20	Fri 16/10/20
59		Draft ITT documentation (Main Contract) for PQQ	13 wks	Mon 20/07/20	Fri 16/10/20
60		EU Advert - Main Contract	0 days	Fri 16/10/20	Fri 16/10/20
61		PQQ period	6.2 wks	Fri 12/03/21	Fri 23/04/21
62		PQQ assessments & report	2 wks	Mon 26/04/21	Fri 07/05/21
63		PQQ notifications	1 wk	Mon 10/05/21	Fri 14/05/21
64		OBC Drafting Period Capaxo	36 days	Mon 15/03/21	Mon 03/05/21
65		Progress Meeting 1	1 day	Thu 15/04/21	Thu 15/04/21
66		LCCC Review 1	10 days	Tue 04/05/21	Mon 17/05/21
67		Workshop 1	1 day	Tue 11/05/21	Tue 11/05/21
68		Final Draft	10 days	Tue 18/05/21	Mon 31/05/21
69		LCCC Review 2	5 days	Tue 01/06/21	Mon 07/06/21
70		Workshop 2	1 day	Tue 08/06/21	Tue 08/06/21
71		Issue Final OBC	3 days	Wed 09/06/21	Fri 11/06/21
72		Presentation to Members (Datw TBC by LCCC)	0 days	Mon 14/06/21	Mon 14/06/21
73		Leisure Committee Approval (Date TBC by LCCC)	0 days	Tue 15/06/21	Tue 15/06/21
74		Capital Committee Approval (Date TBC by LCCC)	0 days	Tue 06/07/21	Tue 06/07/21
75		Full Council Approval (Date TBC by LCCC)	0 days	Tue 20/07/21	Tue 20/07/21
76		Technical Design and ITT documents - Finalise	45 days	Mon 03/05/21	Fri 02/07/21
77		Ice/ bowling Sub Contractor ITT period	20 days	Mon 02/08/21	Fri 27/08/21
78		Ice/ bowling assessment and reports	10 days	Mon 30/08/21	Fri 10/09/21
79		Ice/ Bowling Client approval	10 days	Mon 13/09/21	Fri 24/09/21
80		Ice/ Bowling ITT notifications	1 day	Mon 27/09/21	Mon 27/09/21
81		Ice/ Bowling Standstill	10 days	Tue 28/09/21	Mon 11/10/21
82		Ice & Bowling selection	1 day	Tue 12/10/21	Tue 12/10/21
83		Finalise MC ITT & BoQ	2 wks	Mon 05/07/21	Fri 16/07/21
84		MC ITT Period	6 wks	Mon 02/08/21	Fri 10/09/21
85		MC ITT assessments & report	2 wks	Mon 13/09/21	Fri 24/09/21
86		MC Client approval to award	2 wks	Mon 27/09/21	Fri 08/10/21
87		MC ITT notifications	2 days	Mon 11/10/21	Tue 12/10/21
88		MC 10 day standstill	10 days	Wed 13/10/21	Tue 26/10/21
89		MC Contract award	1 day	Wed 27/10/21	Wed 27/10/21
90		Mobilisation	2 wks	Thu 28/10/21	Wed 10/11/21
91		**RIBA Stage 5**	**632 days**	**Thu 11/11/21**	**Fri 12/04/24**
92		Stage 5 - Construction Ph 1 (incl carpark)	12.2 wks	Thu 11/11/21	Thu 03/02/22
93		Stage 5 - Construction Ph 2 (construction of new building)	84 wks	Fri 04/02/22	Thu 14/09/23
94		Commissioning & float	4 wks	Fri 15/09/23	Thu 12/10/23
95		Stage 5 - Construction Ph 3 (demo of ext building and landscape)	26 wks	Fri 13/10/23	Thu 11/04/24
96		Contract Completion & handover	1 day	Fri 12/04/24	Fri 12/04/24
97		**RIBA Stages 6 & 7**	**260 days?**	**Mon 15/04/24**	**Fri 11/04/25**
98		Stage 6 & 7 - handover & in use	52 wks	Mon 15/04/24	Fri 11/04/25
99					
100		Programme Assumes that Planning has been			
101		received and all outstanding issues clarified
